Studio

Execution plan


Every step of building out one container studio, in order: the carpenter's drawings with their measurements in millimetres, and the steps where the electrician and the plumber come in.

Status: revision A2, 2026-10-28, PRELIMINARY. Measure first (Before you start): the workshop cuts nothing before revision B.

The two studios are the same, so one plan serves both.

Kinyarwanda: soma iyi gahunda mu Kinyarwanda · Print: this plan as a PDF · The studio drawn: the studio page · Its other pages: materials, electric, plumbing


At a glance

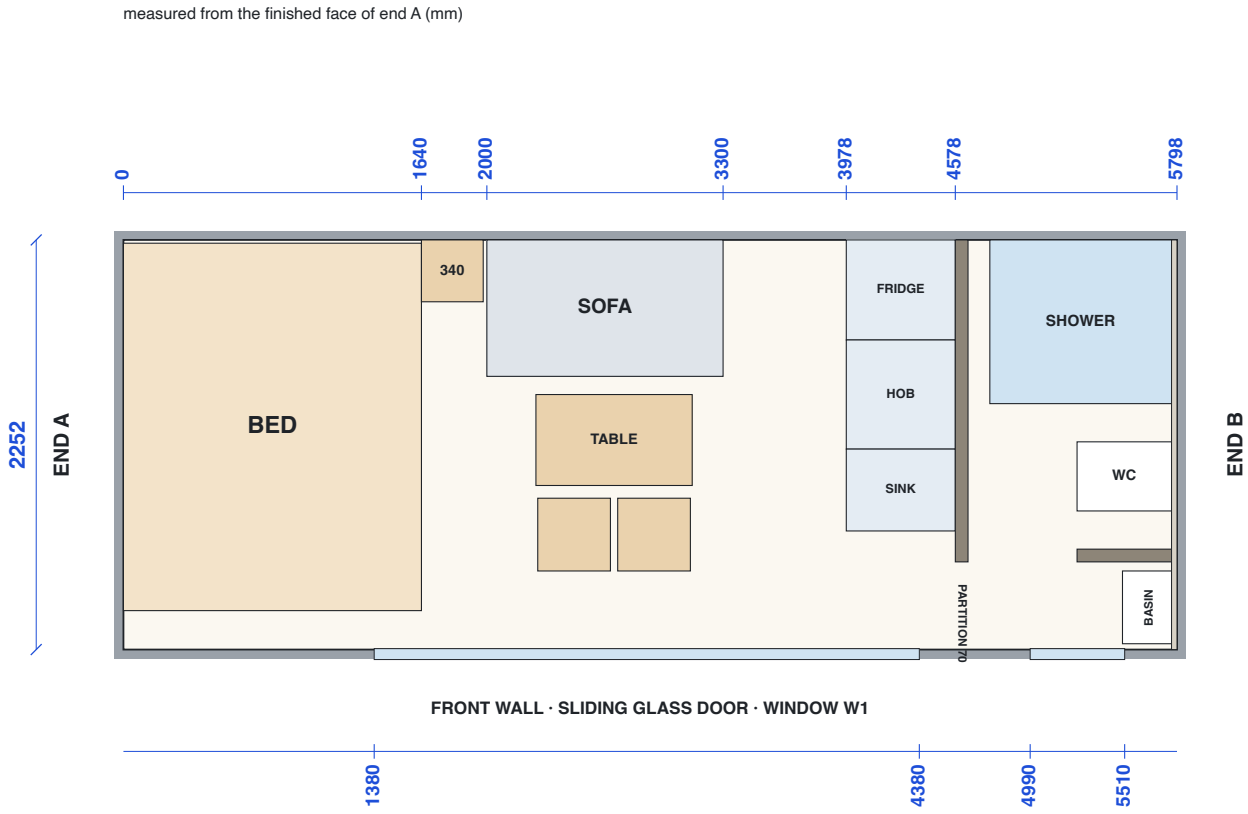

The room from above: every line measured from the finished face of end A · open full size

- The finished room is 5798 long, 2252 wide and 2316 high.
- End A is the closed end, by the bed; end B is the bathroom end.

- One studio costs about RWF 16.6M with its contingency, before the farm's shared septic, water and power works (about RWF 4.9M for both studios) [A: placeholders until three quotes per line, see materials].

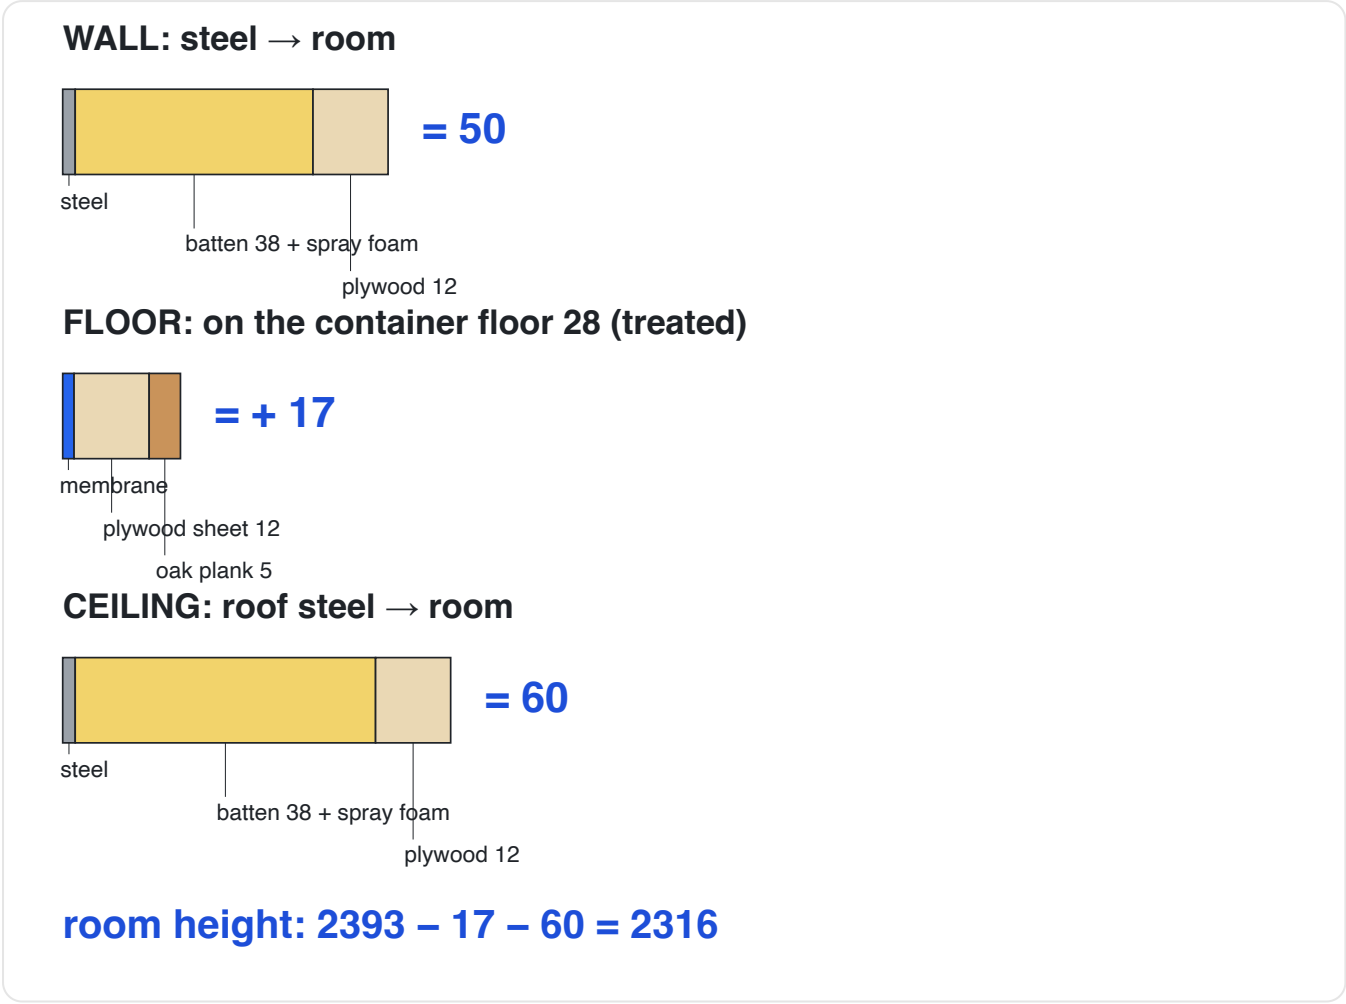

The layers: wall 50, floor 17, ceiling 60 · open full size

Sleep

A queen bed up to 1.6 × 2.0 m against the wall, with two storage boxes underneath, a bedside table, a reading lamp and USB-C.

Cook

A galley on the bathroom wall: under-counter fridge, two-zone induction hob, sink, drinking-water filter. No gas indoors.

Wash

Shower, WC and basin in one row: a wall-hung WC and the shower behind a door, the basin outside it.

Sit

A seating room: a two-seat sofa, a low wide table and two chairs, by the 3 m sliding glass wall onto the deck.


Roof

An open roof terrace with lounge chairs behind a timber-topped rail, up a steel stair; a canopy shades the deck.

Stay cool

The roof deck shades the steel, foam is sprayed onto it inside, a wall fan moves the air, and the AC is ready.

Before you start

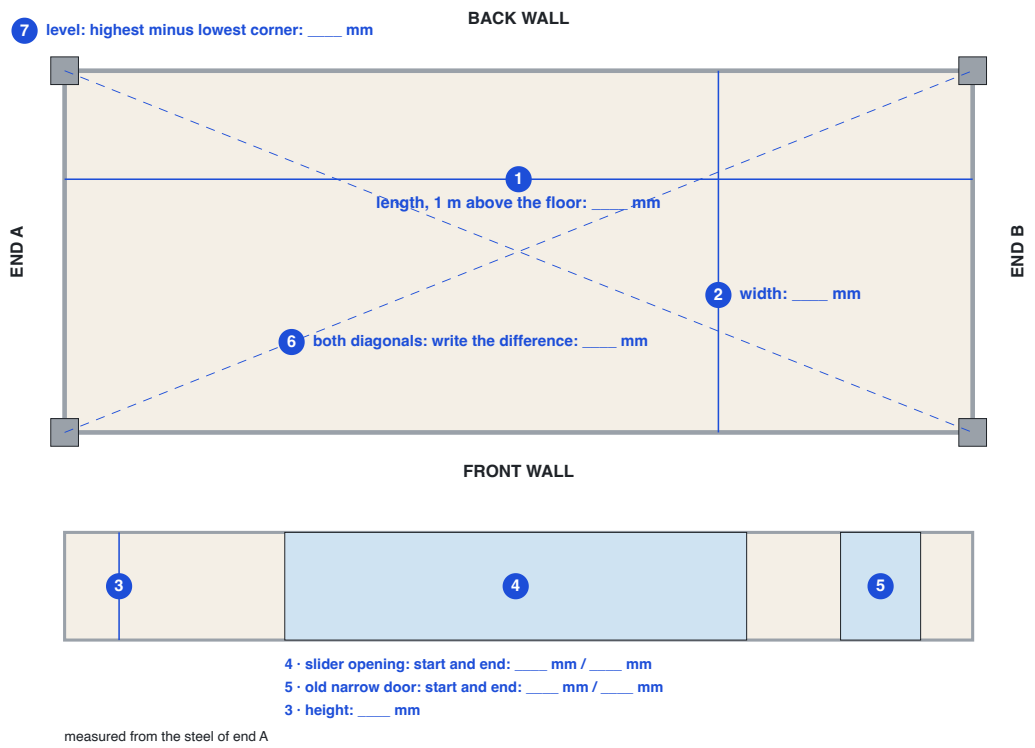


Day 1: measure the 7 numbers and write them on the sheet · open full size

1. Measure both studio containers; mark them U1 and U2 on the doors with chalk.
2. Write the 7 numbers on the survey sheet and send a photo of it the same day.
3. Book the welder: all the hot work comes first, once the supports are level (S01).
4. Have the farm's shared works ready or under way: the septic tank, the storage tank and its booster, the site board and its feeder (the farm's water, the farm's electric).
5. Count every bundle for the studio on site before the first step.

Steps


Floor: membrane and sheets (S02)

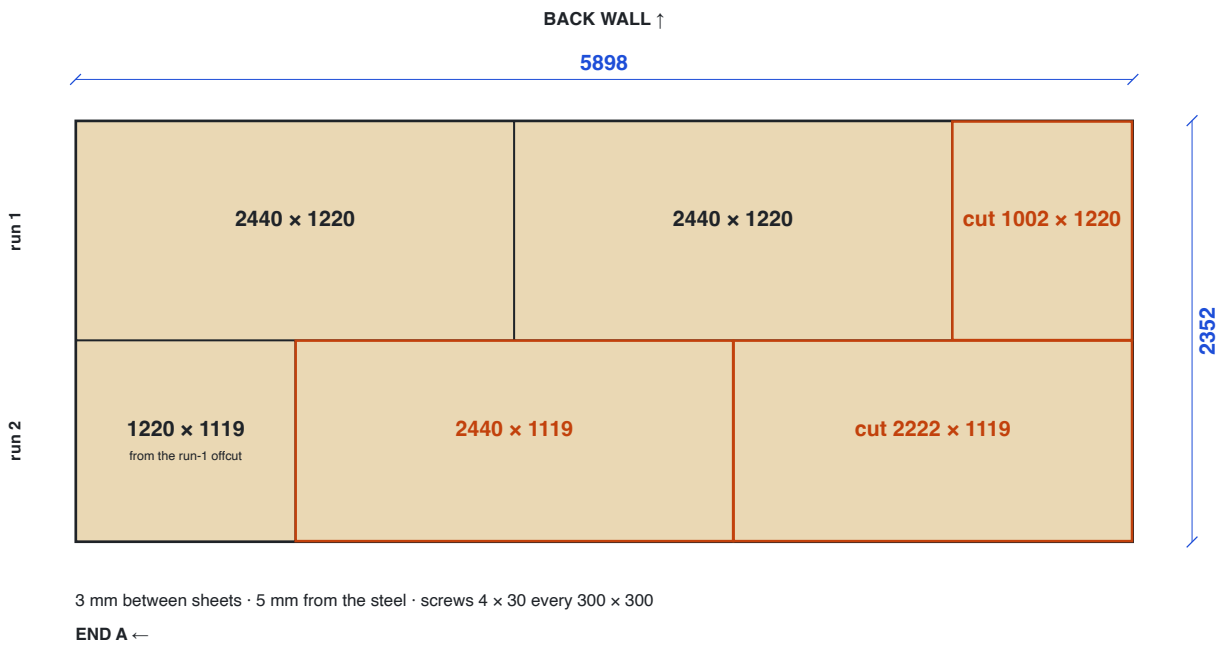


The floor: 5 sheets, the cut ones in red · open full size

1. Finish all the welding first (S01): no welding once the foam is in.
2. Lay the membrane over the old floor, laps 150 mm. Never sand the old floor.
3. Lay the sheets as drawn and screw them down: screws 4 × 30 every 300 mm.


Battens (S03)

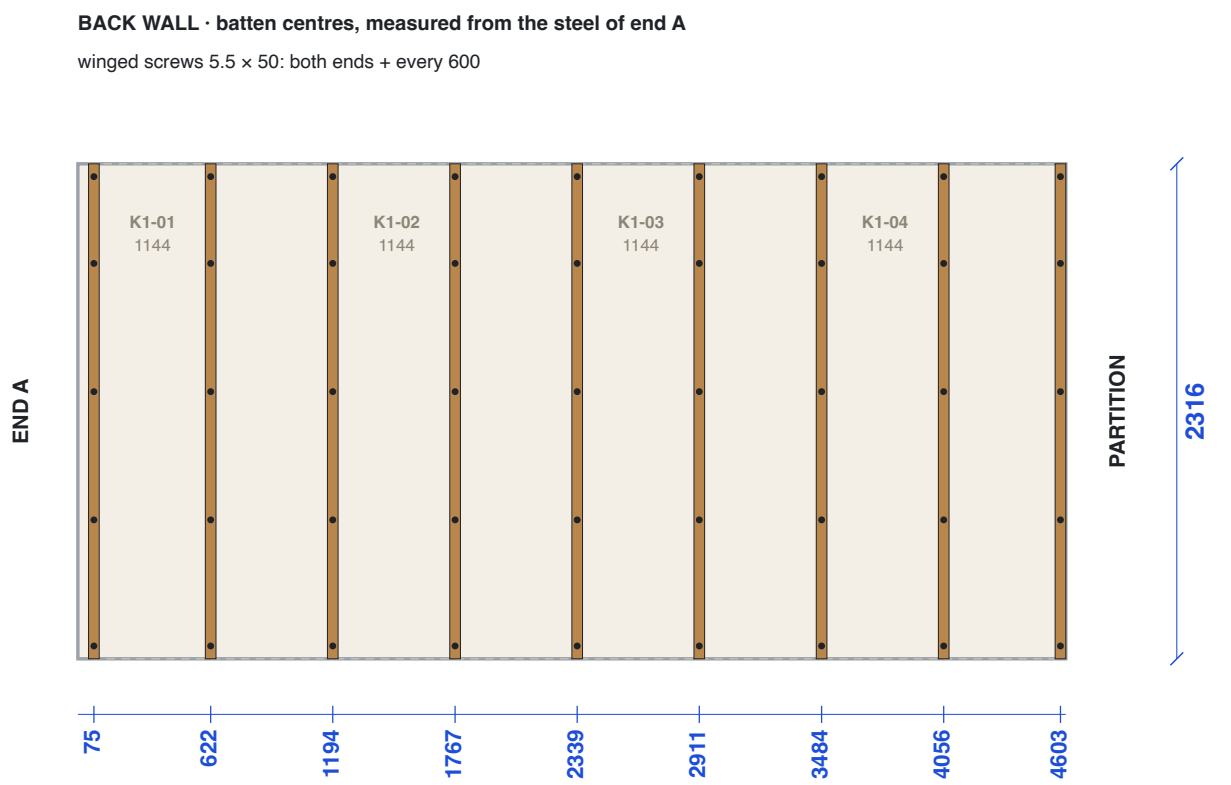

Back wall: the batten centres, measured from the steel of end A · open full size

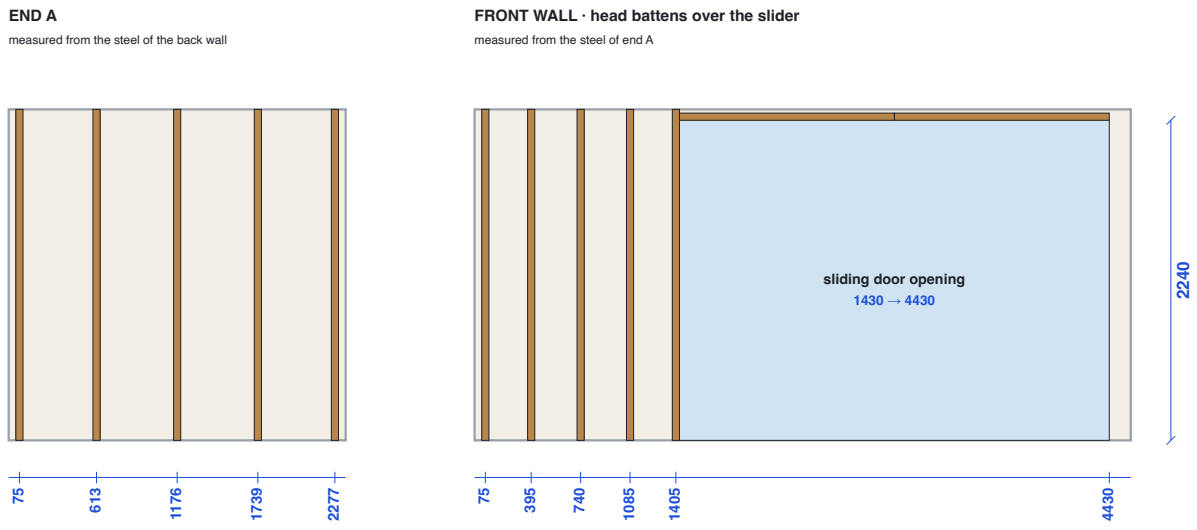

End A, the front wall and the battens over the sliding door · open full size

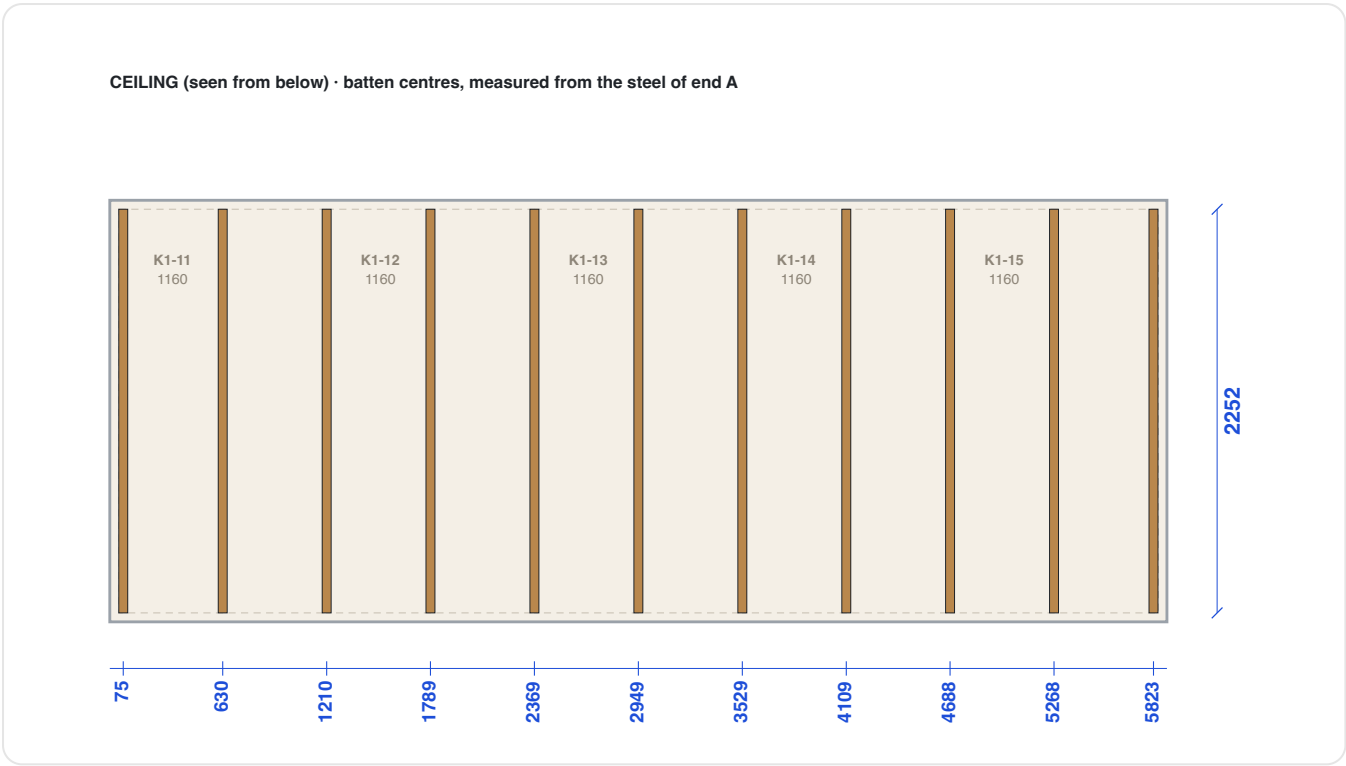


The ceiling: the batten centres, measured from the steel of end A · open full size

1. Battens 38 × 50, standing on the floor sheets.
2. Mark each centre from the steel, at the numbers drawn.
3. Winged screws 5.5 × 50 at both ends and every 600 mm.

Pipes and cables, then foam (S04, S05)

1. The electrician and the plumber put in their cables and pipes (S04): electric, plumbing.
2. The pipes are tested at 10 bar: wait for the signed paper.
3. The foam goes in between the battens; wait 24 hours, then cut it flush.

Lining panels (S05)

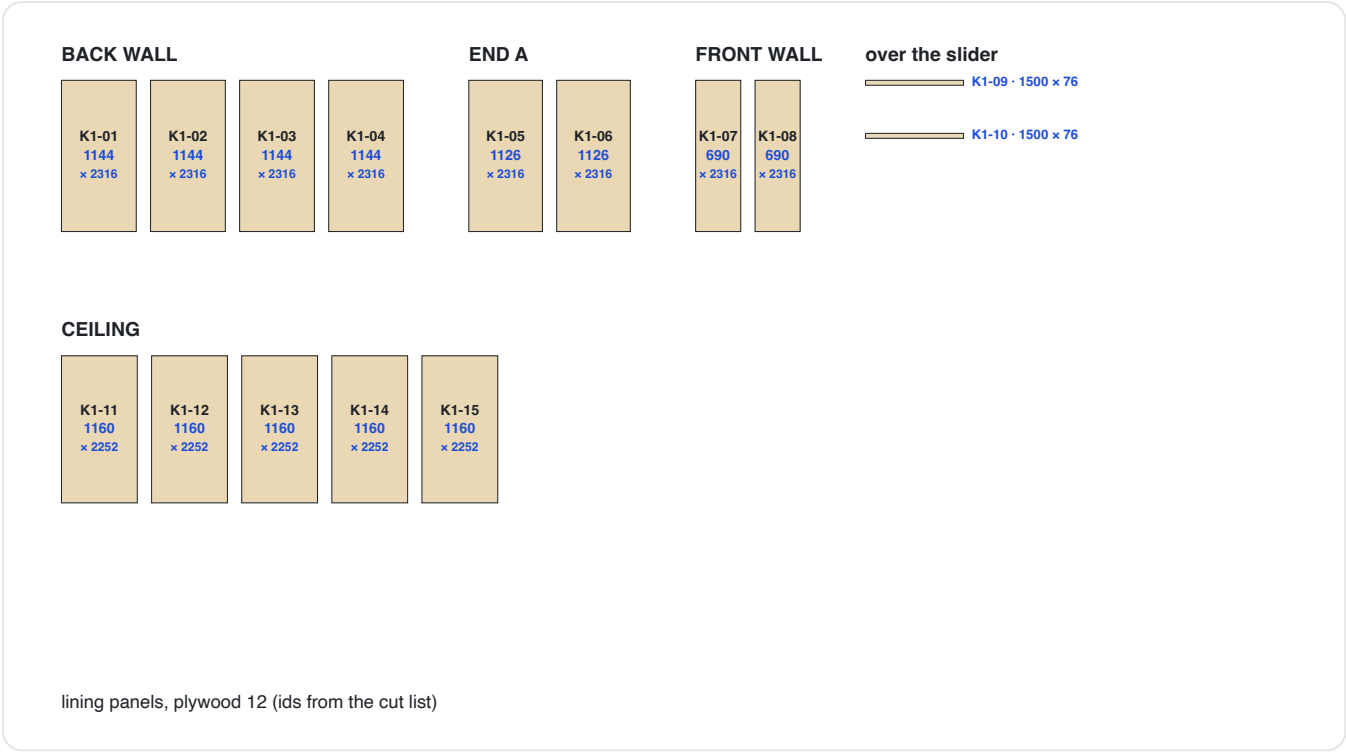


The 15 lining panels with their sizes · open full size

1. The ceiling first, then the walls.
2. Every panel edge sits on a batten centre.
3. Screws 4 × 30: every 200 mm on the edges, every 300 mm in the middle.

Bathroom (S06 to S10)

BATHROOM

measured from the finished face of end A · from the finished back wall

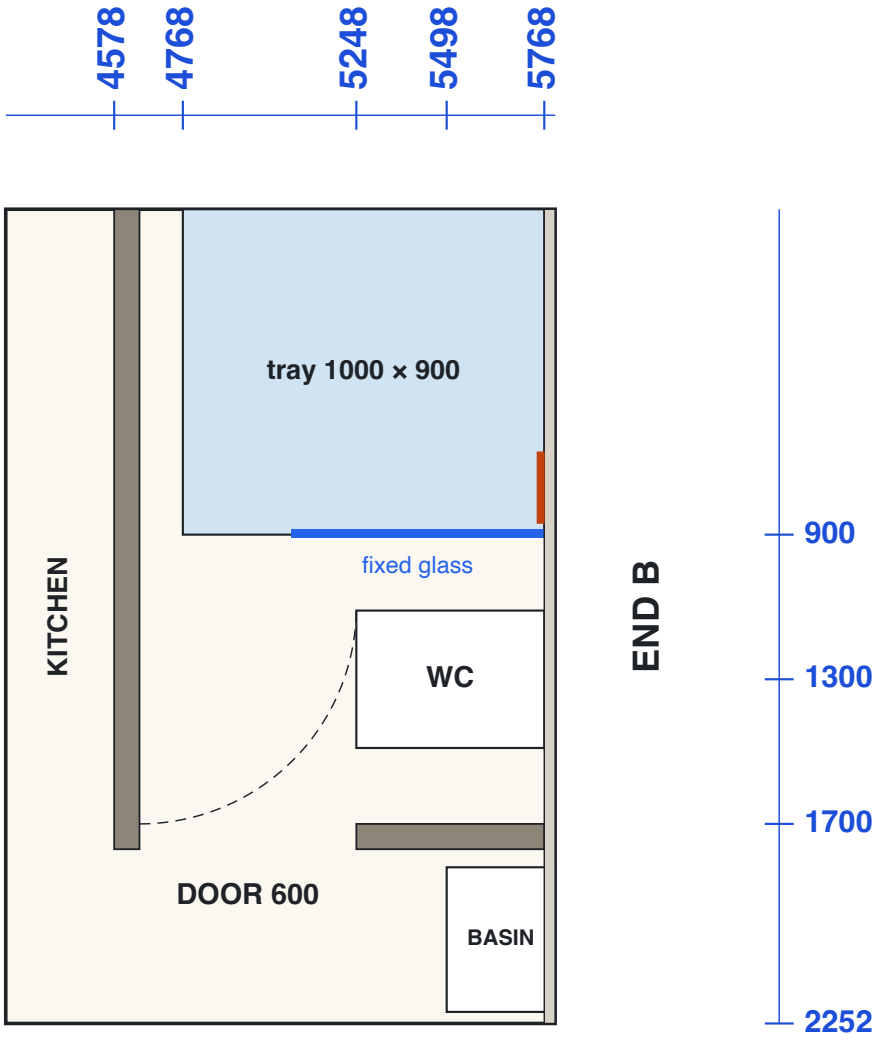


instant heater in the shower: 200 × 330 × 90

WC: 520 × 380 · BASIN: 300 × 400 · fixed glass: 700

The bathroom from above, with every size · open full size

Kitchen (S11 to S14)

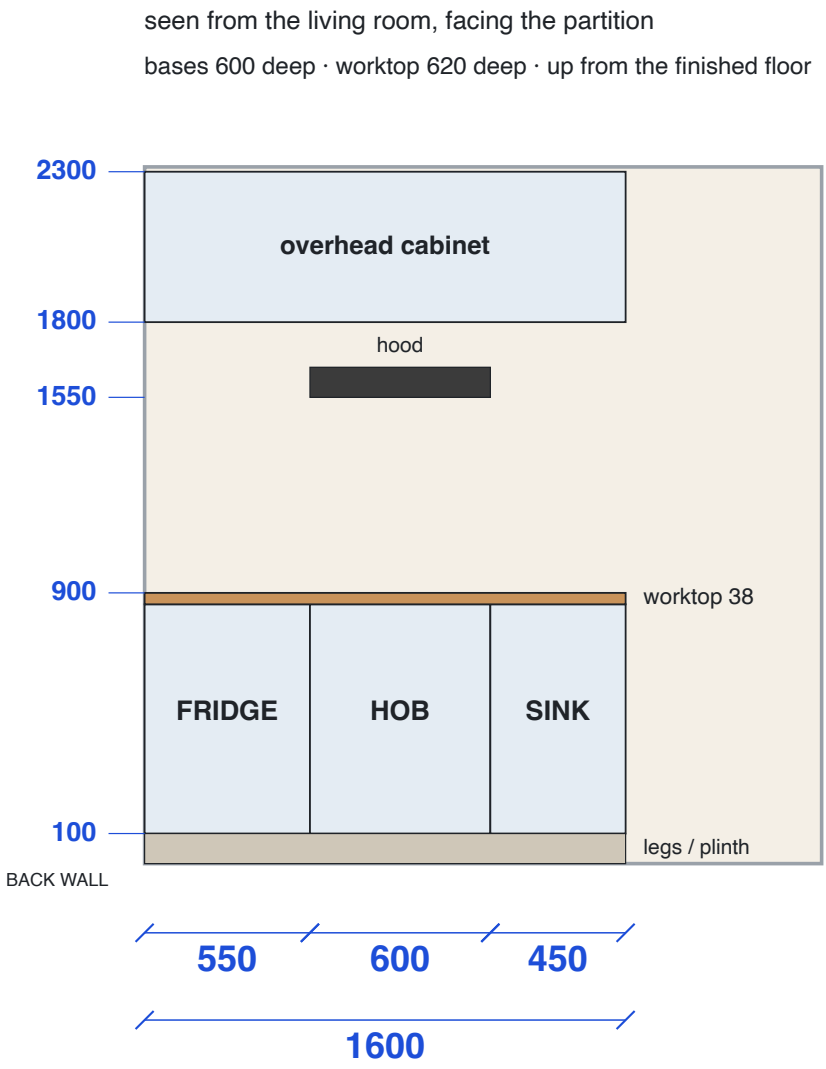

The kitchen, seen from the living room · open full size

1. Lay the oak planks first, from end A to the partition.
2. Then the three bases, the worktop, the overhead cabinet and the hood.

Bed, seating and trims (S15 to S18)

- The bed, the bedside table, the table and chairs and the trims come from the workshop as numbered kits: build each one from its kit sheet.

Second fix, roof and stair (S19 to S27)

1. The electrician's second fix and tests (S19): electric.

2. Bolt the deck beams onto the corner castings, then screw down the deck boards with 5 mm gaps (S20, S21).
3. Bolt the guardrail posts, fix the hardwood top rail and tension the stainless cables (S22, S23).
4. Set the veranda posts and the stair footings; bolt the two flights and the landing (S24, S25).
5. Place the chairs and the side table, then bond the steelwork to earth (S26, S27).

Hold points

1. The measurements are sent → revision B → the workshop cuts.
2. All the welding is done → then the foam.
3. The pipe test has passed → then the foam.
4. The foam has cured for 24 hours → then the panels.
5. The bathroom membrane is checked → then the tiles.
6. A structural engineer has inspected the roof → then guests use the terrace (S27).

Done when

1. The electrical tests pass and the certificate is signed (S19); the pipes held 10 bar before the foam, the drains are fill-tested, and the shower holds about 40 °C at full flow.
2. The doors, the drawers and the bathroom door swing freely; the slider locks; the insect mesh is tight.
3. The farm's septic system has passed its inspection: no guest stays before it (D-016).
4. Each studio is cleaned and photographed, and its measurements are kept with its drawing set.

Open questions

1. Which two containers are U1 and U2? Day 1.
2. Is a welder booked? Before S01.
3. Who sprays the foam? Before S05.
4. Floor sheets 12 mm, or 18 mm if the old floor is more than 5 mm out over 2 m? Before S02.
