Carpenter's guide: the studio interior


Every step of the studio interior as a drawing with its measurements, in millimetres.

Status: revision A2, 2026-10-28, PRELIMINARY. Measure first (step 1): the workshop cuts nothing before revision B.

The two studios are the same, so one guide serves both.

Kinyarwanda: soma aya mabwiriza mu Kinyarwanda · Print: this guide as a PDF


1. Measure the container (Day 1)

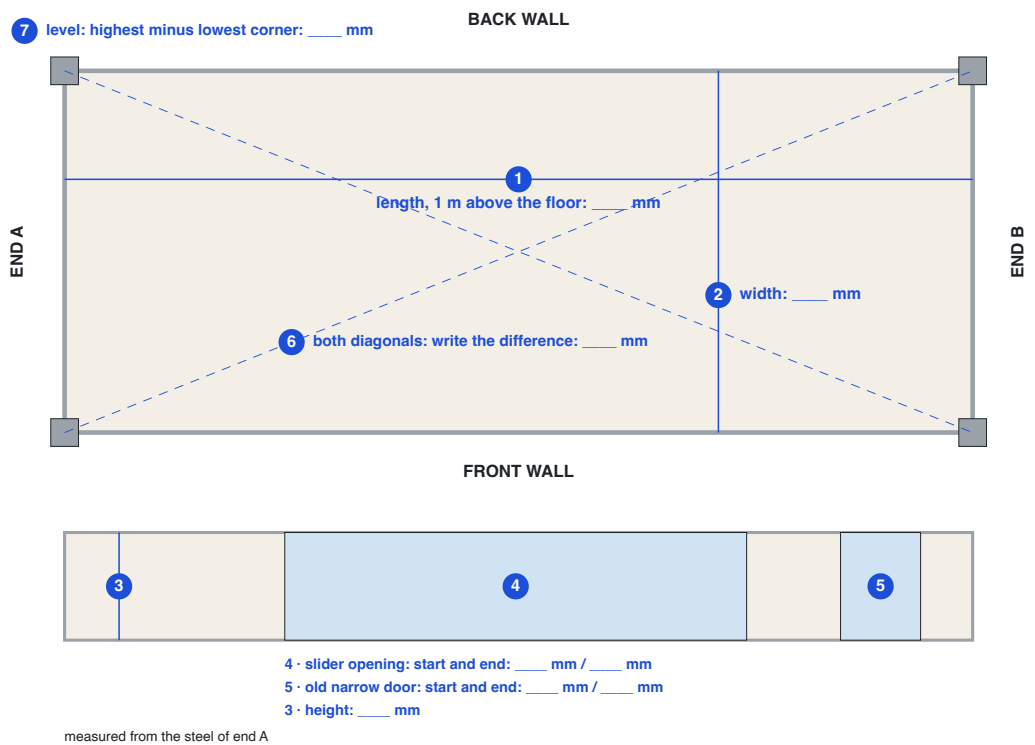

Day 1: measure the 7 numbers and write them on the sheet · open full size

1. Measure both studio containers; mark them U1 and U2 on the doors with chalk.
2. Write the 7 numbers and send a photo of the sheet the same day.


2. The finished room

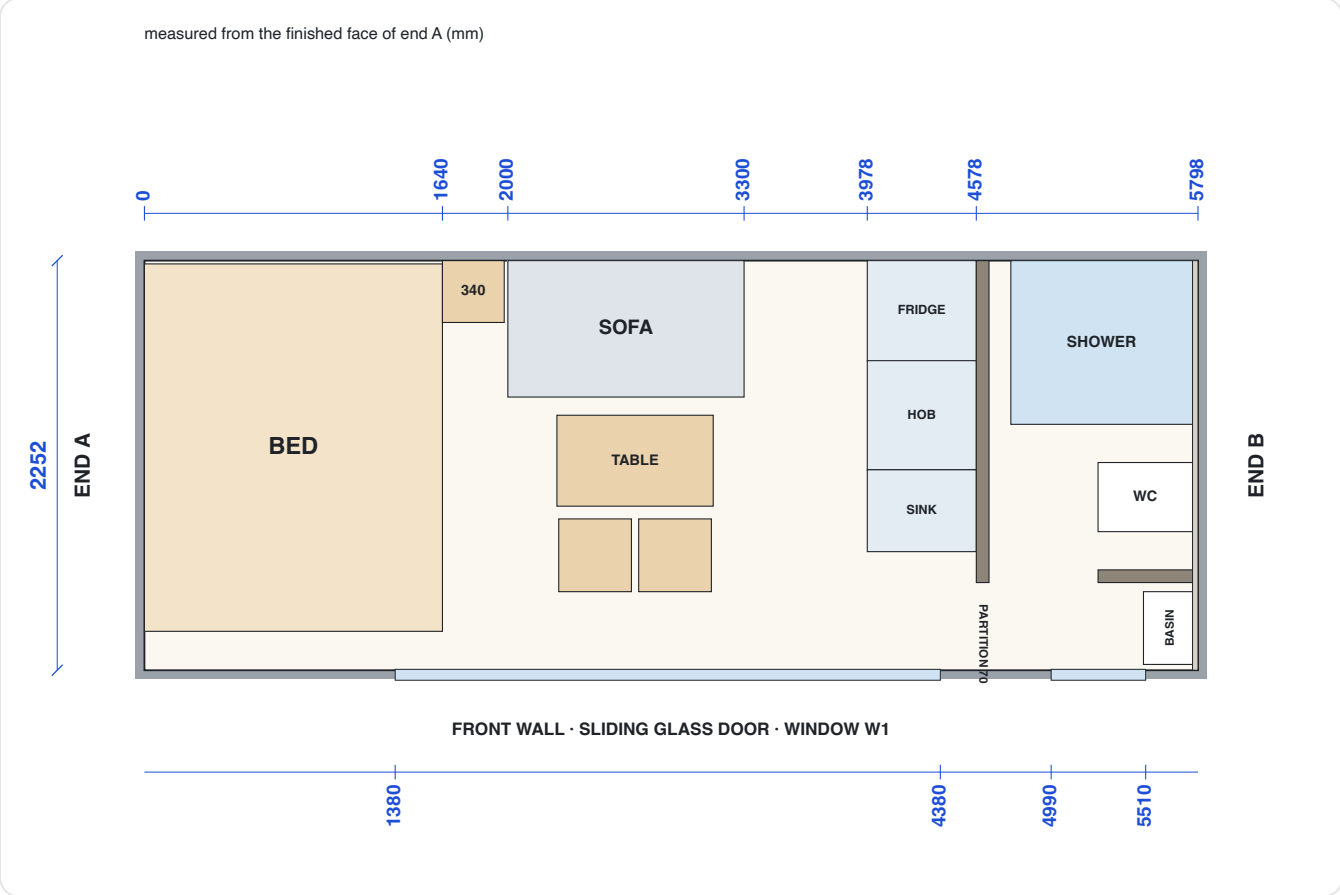

The room from above: every line measured from the finished face of end A · open full size


- The finished room is 5798 long, 2252 wide and 2316 high.
- End A is the closed end, by the bed; end B is the bathroom end.

3. What goes on the steel

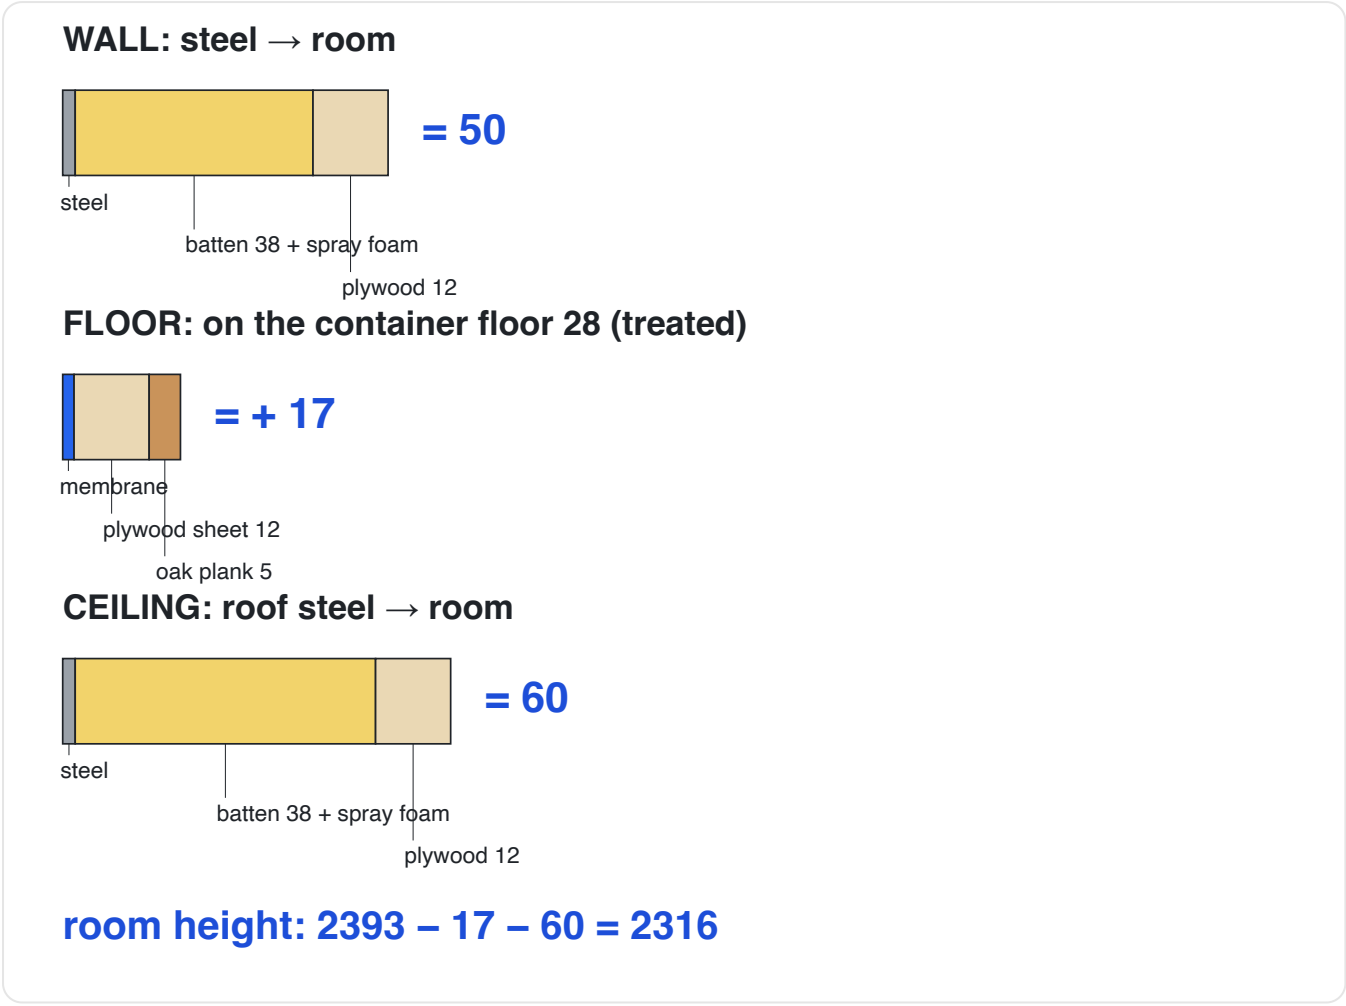

The layers: wall 50, floor 17, ceiling 60 · open full size


4. Floor: membrane and sheets (S02)

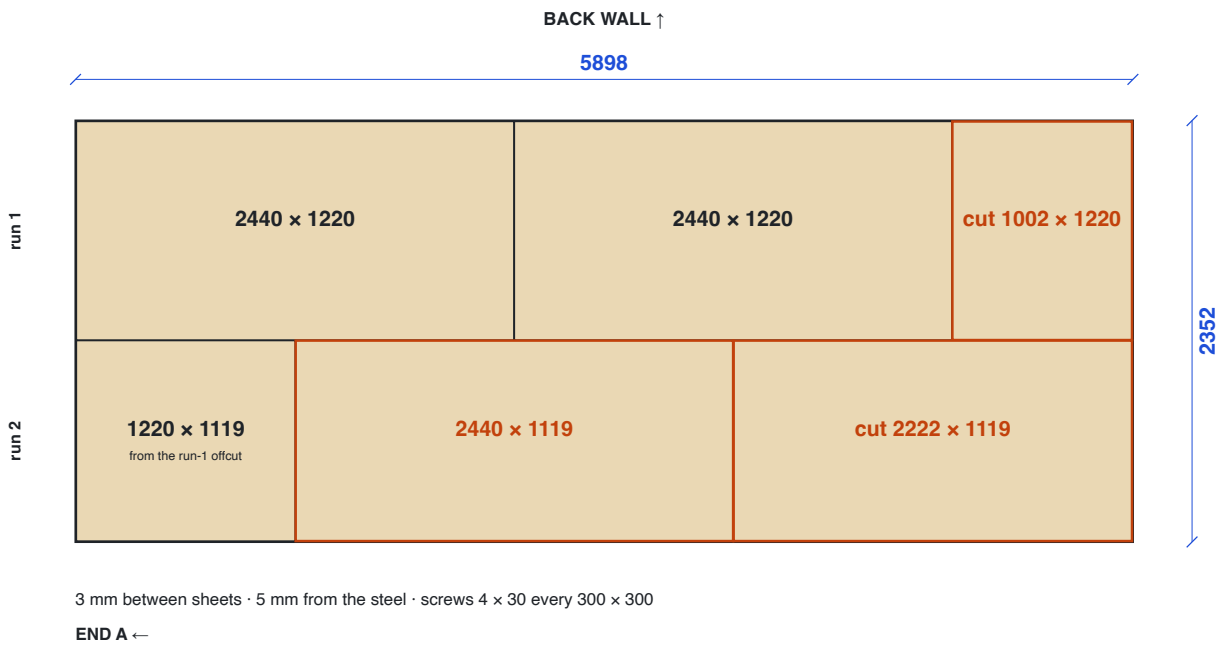


The floor: 5 sheets, the cut ones in red · open full size

1. Finish all the welding first (S01): no welding once the foam is in.
2. Lay the membrane over the old floor, laps 150 mm. Never sand the old floor.
3. Lay the sheets as drawn and screw them down: screws 4 × 30 every 300 mm.


5. Battens (S03)

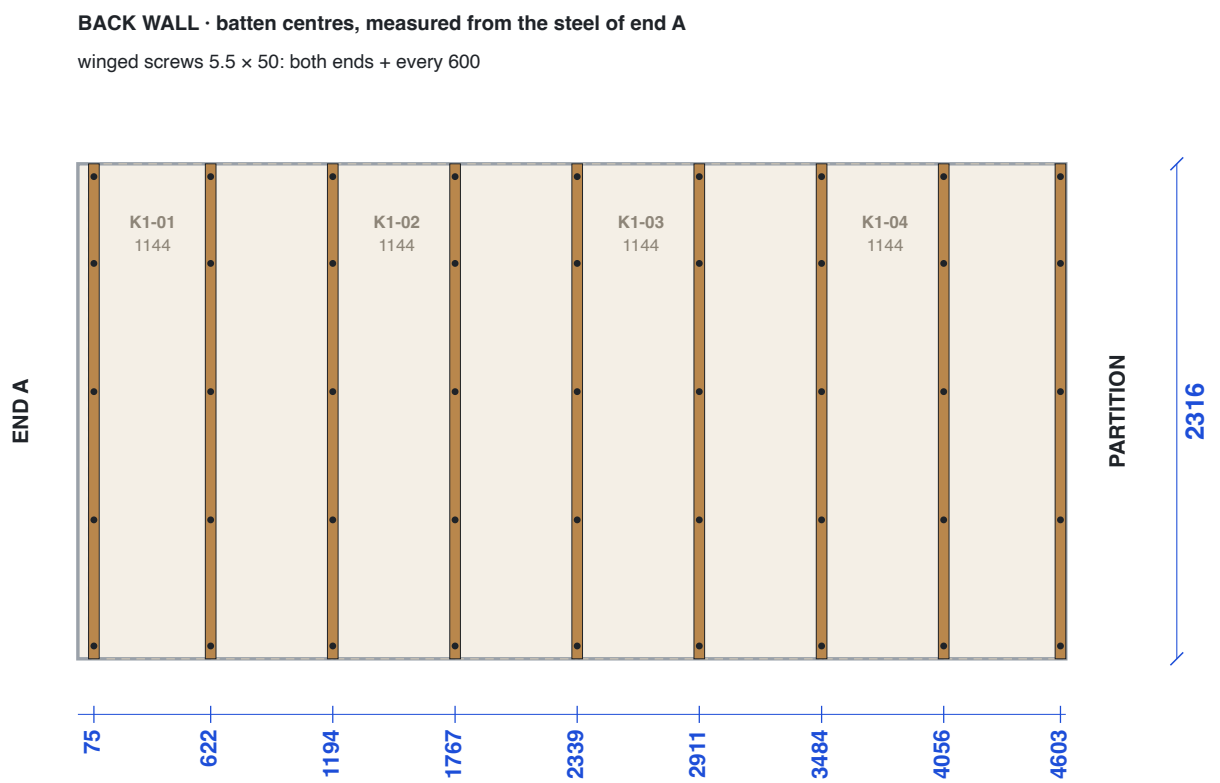

Back wall: the batten centres, measured from the steel of end A · open full size

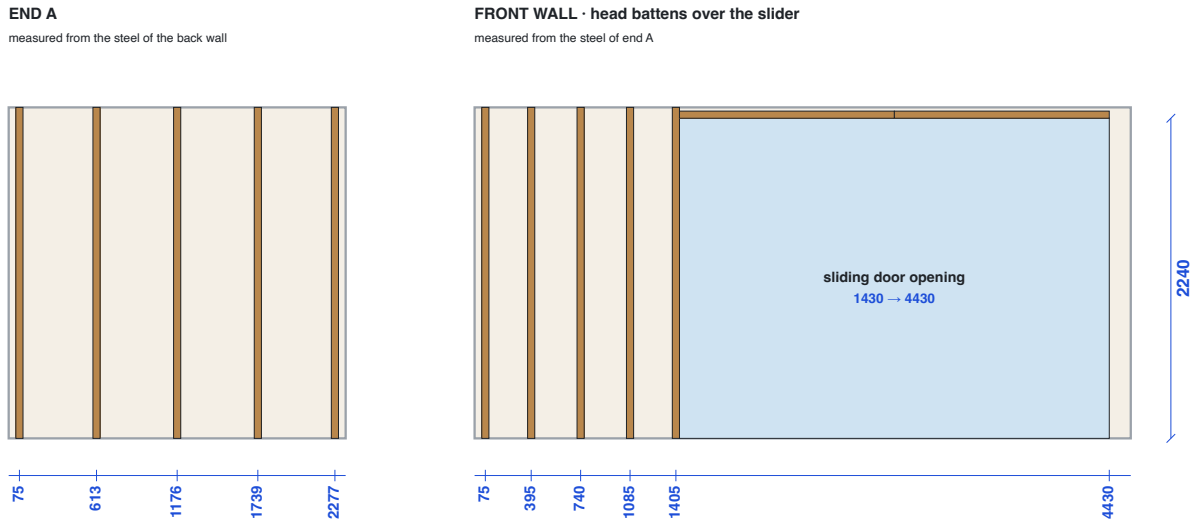

End A, the front wall and the battens over the sliding door · open full size

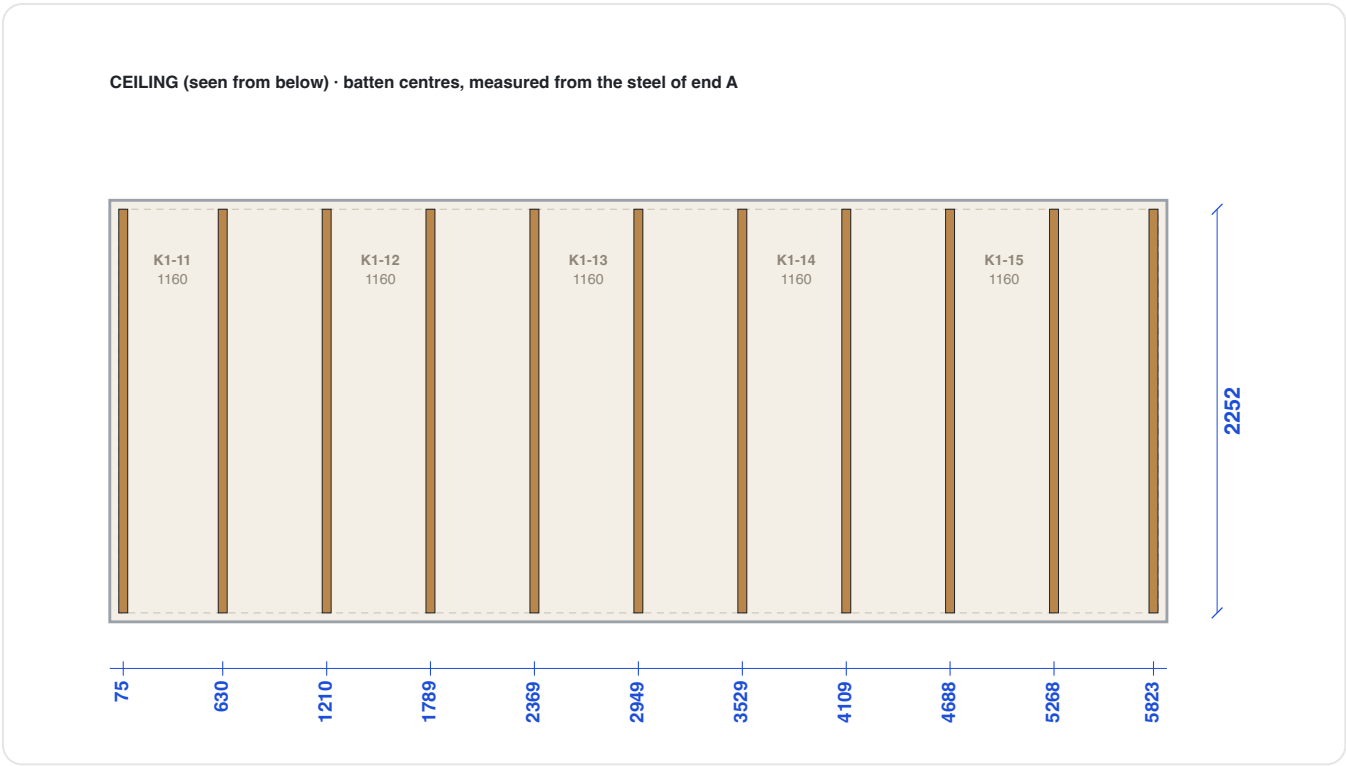


The ceiling: the batten centres, measured from the steel of end A · open full size

1. Battens 38 × 50, standing on the floor sheets.
2. Mark each centre from the steel, at the numbers drawn.
3. Winged screws 5.5 × 50 at both ends and every 600 mm.

6. Pipes and cables, then foam (S04, S05)

1. The electrician and the plumber put in their cables and pipes (S04).
2. The pipes are tested at 10 bar: wait for the signed paper.
3. The foam goes in between the battens; wait 24 hours, then cut it flush.

7. Lining panels (S05)

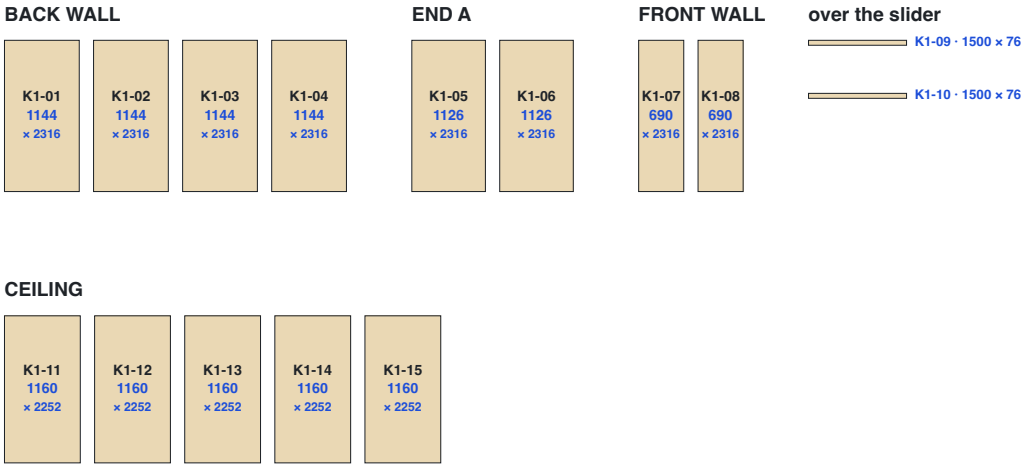

lining panels, plywood 12 (ids from the cut list)


The 15 lining panels with their sizes · open full size

1. The ceiling first, then the walls.
2. Every panel edge sits on a batten centre.
3. Screws 4 × 30: every 200 mm on the edges, every 300 mm in the middle.

8. Bathroom (S06 to S10)

BATHROOM

measured from the finished face of end A · from the finished back wall

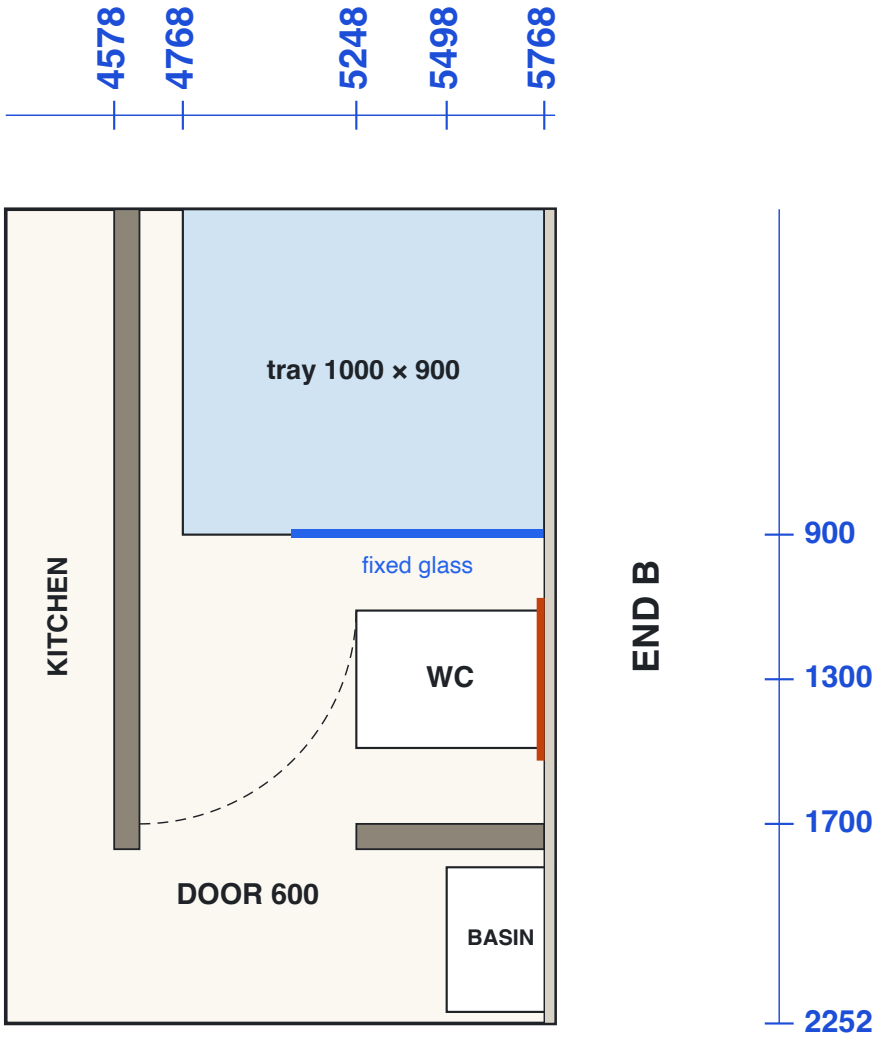


30 L heater box above the WC: 450 × 450 × 300

WC: 520 × 380 · BASIN: 300 × 400 · fixed glass: 700

The bathroom from above, with every size · open full size

9. Kitchen (S11 to S14)

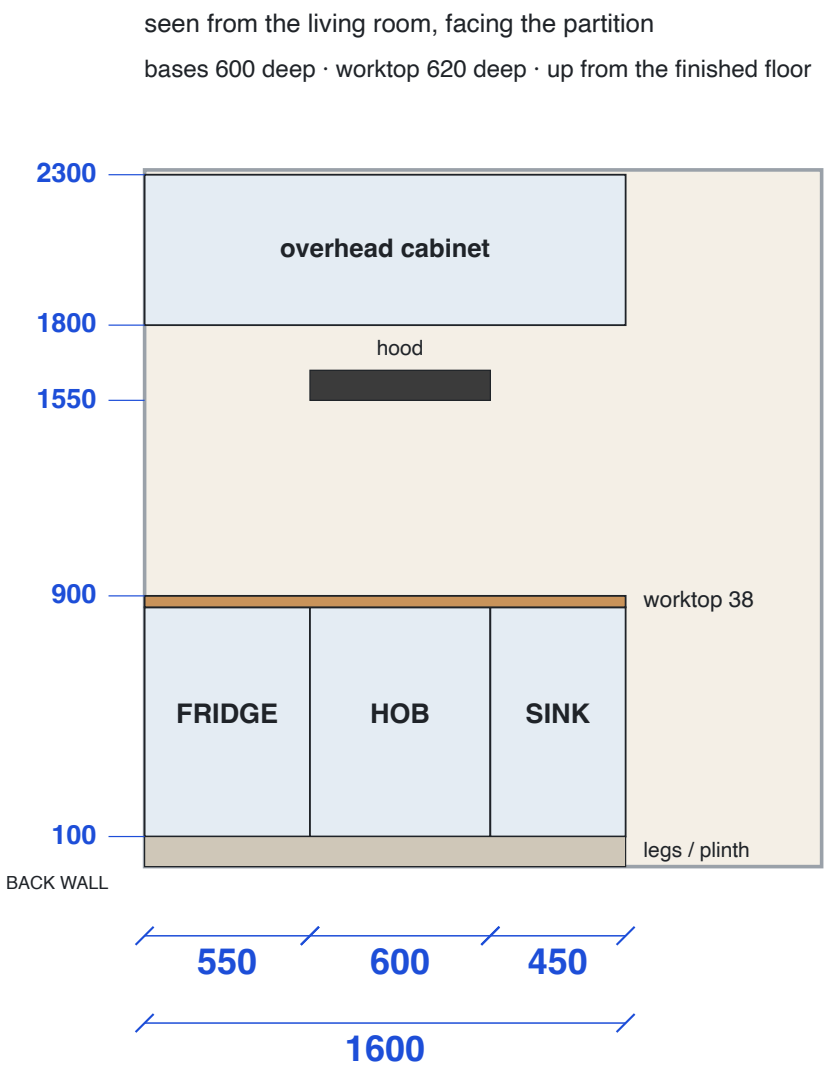

The kitchen, seen from the living room · open full size

1. Lay the oak planks first, from end A to the partition.
2. Then the three bases, the worktop, the overhead cabinet and the hood.

10. Bed, seating and trims (S15 to S18)

- The bed, the bedside table, the table and chairs and the trims come from the workshop as numbered kits: build each one from its kit sheet.

11. Stop and check

1. The measurements are sent → revision B → the workshop cuts.
2. All the welding is done → then the foam.

3. The pipe test has passed → then the foam.
4. The foam has cured for 24 hours → then the panels.
5. The bathroom membrane is checked → then the tiles.

12. What to buy, per studio

Item	Quantity
Plywood 12, sheets 2440 × 1220, floor	5
Plywood 12, sheets 2440 × 1220, linings	15
Plywood 18, sheets 2440 × 1220	8
Marine plywood 18, sheets 2440 × 1220 (bathroom)	3
Worktop blank 38, 3050 × 650	1
Treated battens 38 × 50, 2.4 m long	32, plus 10% spare
Polythene membrane 250 µm	15.3 m²
Oak planks 5 with underlay	11.1 m²
Spray foam, by the contractor	34.9 m²
Winged screws 5.5 × 50	192
Wood screws 4 × 30, floor and linings	189 + 600
Concrete block stands 40 × 60 cm	4

The full list with prices is the bill of materials; every part's size is in the cut list.

13. Questions before the step named

1. Which two containers are U1 and U2? Day 1.
2. Is a welder booked? Before S01.
3. Who sprays the foam? Before S05.
4. Floor sheets 12 mm, or 18 mm if the old floor is more than 5 mm out over 2 m? Before S02.
